


# MASTER WORKSHOP WEBINAR: PROVING & PRICING EXTENSION OF TIME CLAIMS (QUANTUM)

A PRACTICAL, WORKSHOP BASED INTENSIVE TUTORIAL WHICH WILL LOOK AT ALL KEY ASPECTS RELATED TO EOT CLAIMS

OUR WEBINARS ARE DESIGNED TO GIVE YOU TANGIBLE BENEFITS

A HEAD OFFICE OVERHEAD CLAIMS CALCULATOR IN MS EXCEL WILL BE PROVIDED TO ALL ATTENDEES

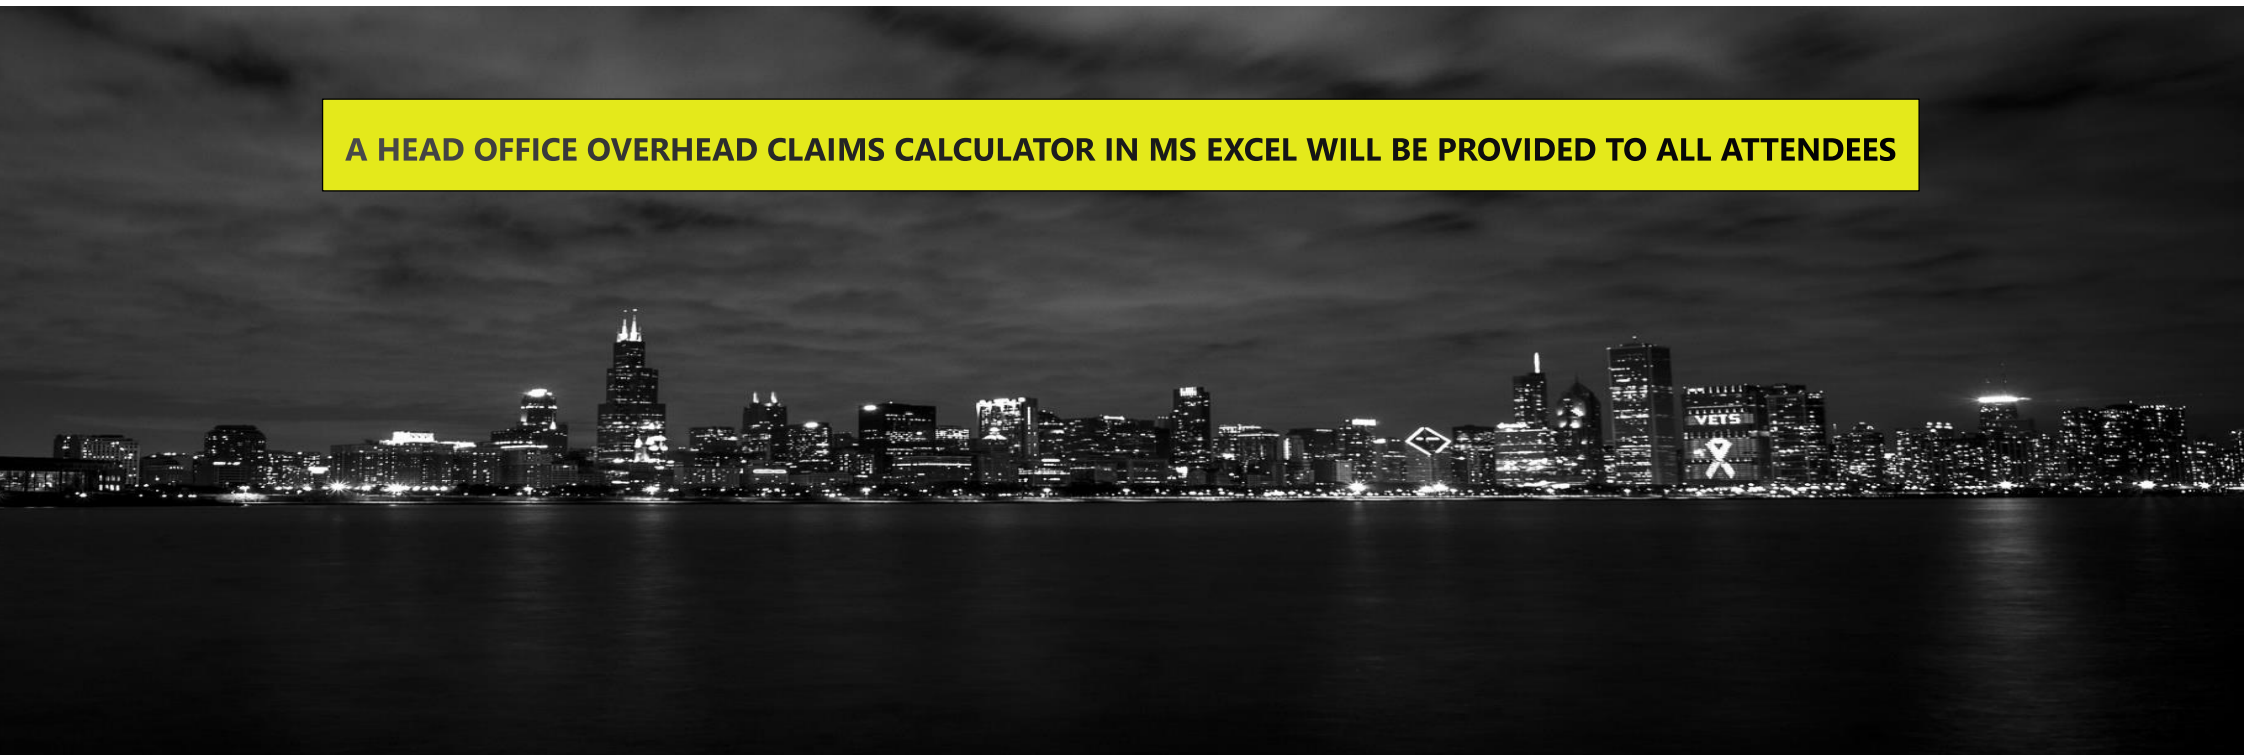

Date: 13th July, 2017

Time: 09:30 hrs. (CET, GMT +2)

Duration: ca. 2 hours

Attendance Fee: 24.99 GBP (British Pounds)

Presenter: N.M. Raj

Available Delegate Slots: Limited

Calculating Quantum for an EOT claim is a complex task

In this premium webinar, N.M. Raj will train attendees on all major claim headings related to this specialism.

Guidance will also be provided on how to avoid critical errors which may seriously jeopardise an EOT claim

**TO REGISTER, PLEASE CLICK [HERE](#)**

## TOPICS COVERED

**Introduction:** EOT claims and Prolongation Costs

**Claim Headings:** A review of the main headings related to EOT Claims

**Case-Studies:** Detailed and practical case-studies from N.M. Raj's projects

**Key Errors to avoid:** If prolongation costs are calculated incorrectly, they can result in substantial losses for the Contractor or they could also be rejected during dispute resolution

**Master Workshops: Calculation of Quantum** - A detailed demonstration (**Delegates are required to have laptops with MS Excel**)


**Calculation of Head Office Overheads** – A review of all major techniques to successfully claim for this heading (includes reference to case law) - A head office overhead claims calculator in Ms Excel will be provided to all attendees

**Template for creating an EOT claim:** Attendees will receive several fully detailed workshops on how to prepare prolongation cost claims in MS Excel which they can use as a template to create new claims on their projects

**Template for Claims Narrative:** Preparing the claims narrative for an EOT claim with prolongation costs included

**Strategies for EOT Claims:** Preparation and Defence

## EXCERPTS FROM THE MASTER WORKSHOP WEBINAR (HANDOUTS)

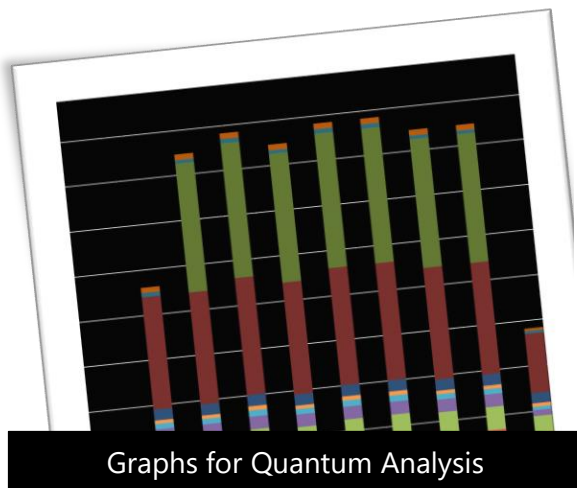

**THE CONTRACTOR'S CLAIM FOR AN  
EXTENSION OF TIME AND RECOVERY OF  
INCURRED COSTS**

BASED ON THE CONTRACT AGREEMENT

Between  
XXXXXX  
(the Employer)  
And  
XXXXXX  
(the Contractor)

Sample EOT Claim Template in MS Word

Event	Category of	Cause	Effect	Impact (Y/N)
Design				
Delay in issuing design to the Sub-Contractor	Contractor	Contractor's Designer is making mistakes	Delay in issuing design to the Sub-Contractor	Y
Design Late by the Contractor's Designer	Contractor	Contractor's Designer did not complete the design	Delay to the Sub-Contractor's works	Y
Incomplete Design by the Contractor's Designer	Contractor	Contractor's Designer's error	Delay to the Sub-Contractor's works	Y
Error in Design - Co-ordination error by the Contractor's Designer	Contractor	Contractor's Designer's error	Delay to the Sub-Contractor's works	Y
Procurement				
Contractor's Procurement Delay - Knock-on Delay To Sub-Contractor	Contractor	Contractor's delay in Procuring another sub-contract package resulting in knock-on delays to the Sub-Contractor	Delay in procuring Sub-Contractor and awarding contract, knock-on delay for Sub-Contractor on site	Y
Contractor's delay in providing free issue material to the Sub-Contractor	Contractor	Contractor could not get a material supplier approved & this results in knock-on delays to the Sub-Contractor	Delay in procuring supplier and awarding contract, knock-on delay for Sub-Contractor on site	Y
Contractor's Delay in awarding a Contract to another Sub-Contractor	Contractor	Contractor's Delay in awarding a Contract to another Sub-Contractor	Delay to Sub-Contractor's Mobilisation on a section of the site, knock-on delay for Sub-Contractor on site	Y
Contractor's Delay - awarding another sub-contract package	Contractor	Contractor's Delay in awarding a Contract to another Sub-Contractor	Delay to Sub-Contractor's Mobilisation on a section of the site, knock-on delay for Sub-Contractor on site	Y

EOT Workshop

## WHO SHOULD ATTEND?

This Master Workshop is essential for all professionals operating in the real estate & construction industry including contractors, investors, engineers, lawyers, consultants, bankers, insurers and others involved on construction projects

## ADDITIONAL BENEFITS

Attendees will acquire 2 hours of CPD/PDU.

All attendees will receive a 25% discount to N.M. Raj's internationally renowned Online Master Course in Construction Claims

## IMPORTANT NOTES ABOUT REGISTRATION

Please Click on this link to register for this event:

Our Webinars are fully reserved very quickly, so, please book early!

**Attendees are required to have laptops with MS Excel & MS Word; this is necessary to solve workshops**

Delegates who have purchased our Online Master Course in Construction Claims are requested not to register. This topic is already covered in a module which forms part of the Online Master Course

